




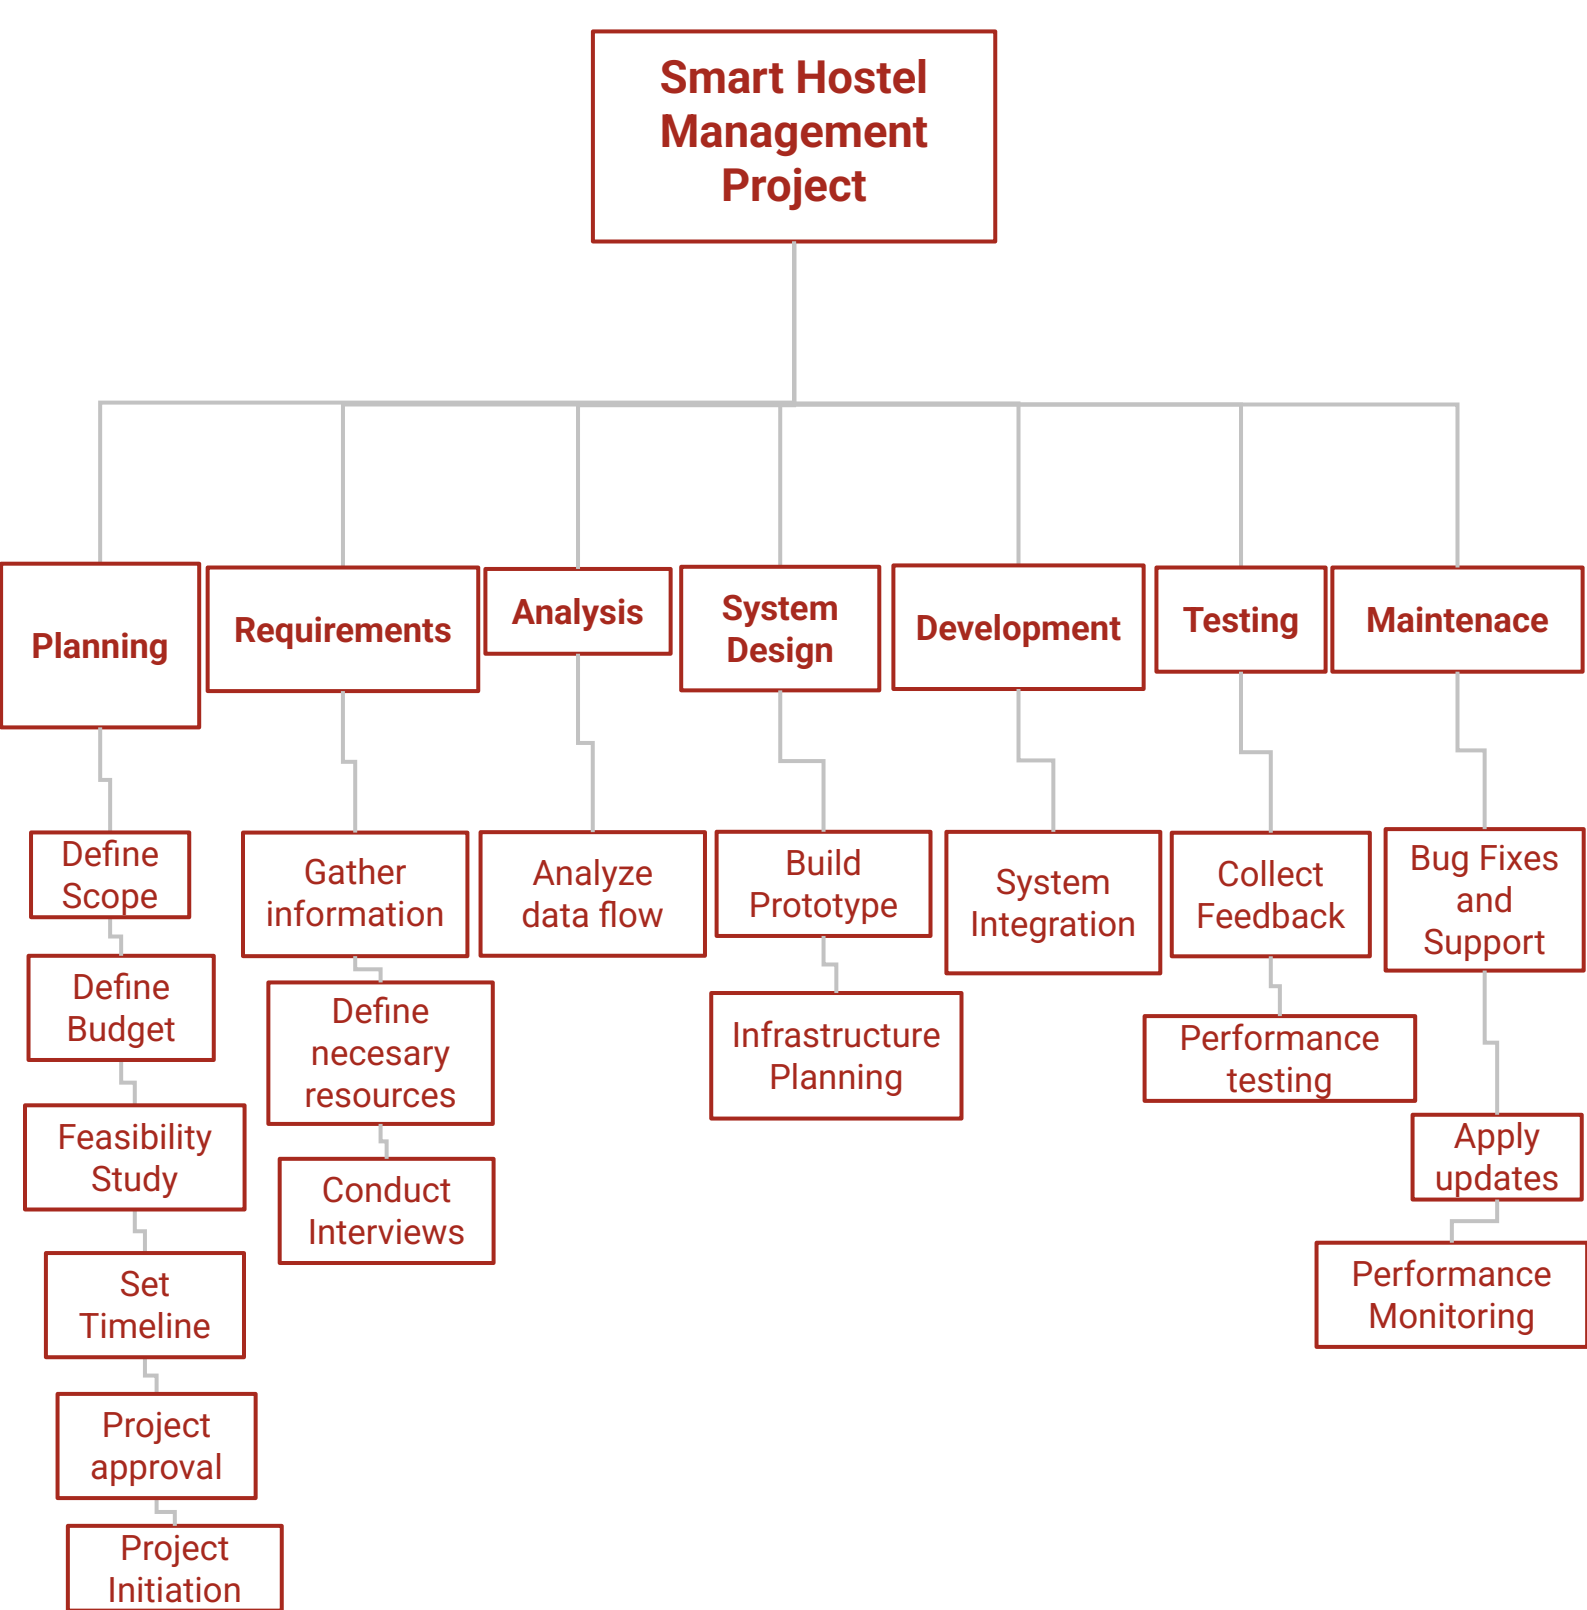

	Tasks	Predessecor	Duration
A	Define Scope	None	3 days
B	Feasibility Study	A	6 days
C	Project Approval	B	3 days
D	Define Budget	C	4 days
E	Set Timeline	D	2 days
F	Project Initiation	E	1 day
G	Gather Information	F	7 days
H	Define Necessary Resources	G	4 days
I	Conduct interviews	G	5 days
J	Analyze Data Flow	H, I	5 days

	Tasks	Predecessor	Duration
K	Build Prototype	J	10 days
L	Infrastructure Planning	J	8 days
M	System Integration	K, L	7 days
N	Collect Feedback	K	7 days
O	Performance Monitoring	M	8 days
P	Performance Testing	M	6 days
Q	Bug Fixes and Support	N, P, O	7 days

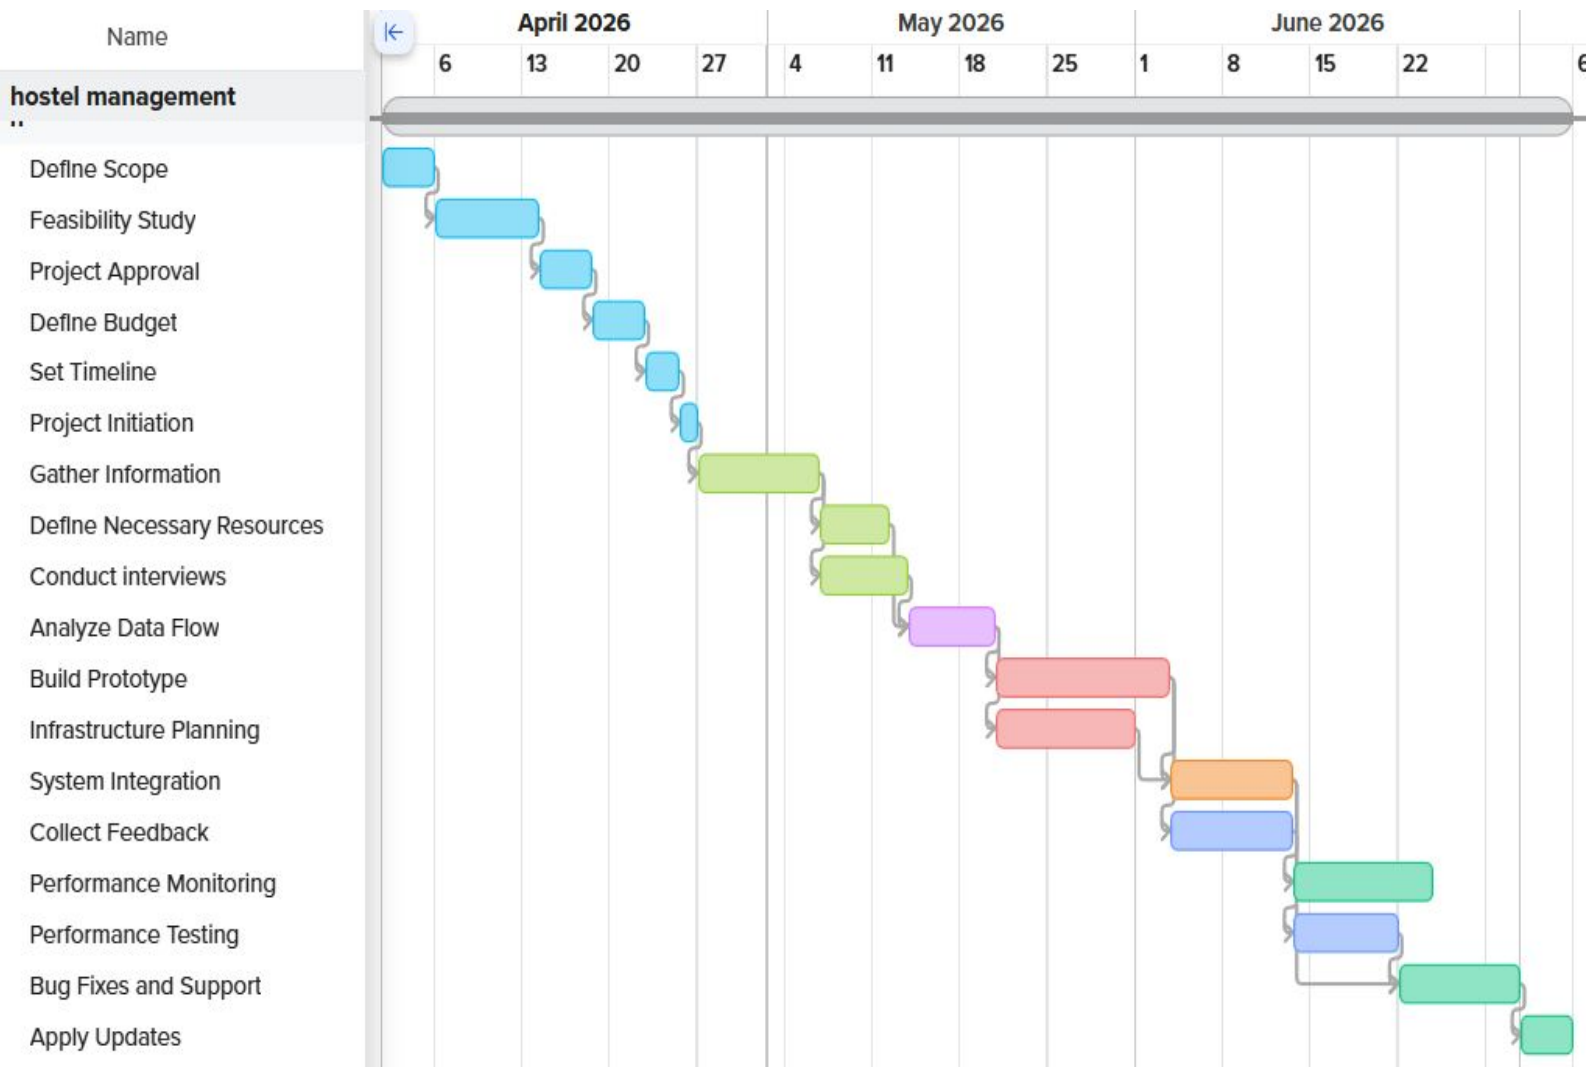

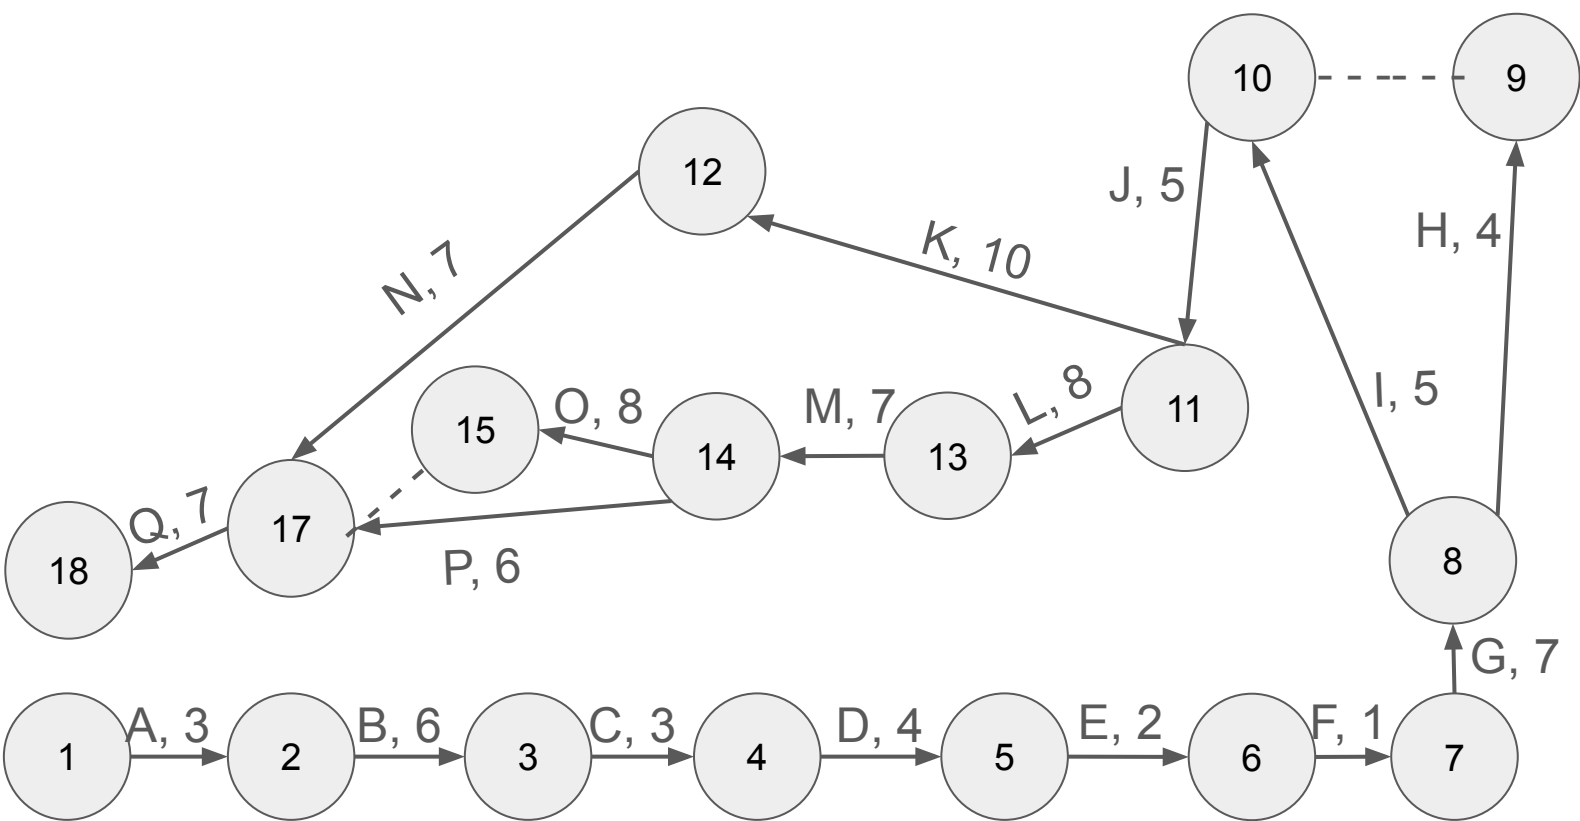

Path 1: A, B, C, D, E, F, G, H, J, K, N, Q = 59

Path 2: A, B, C, D, E, F, G, I, J, K, N, Q = 60

Path 3: A, B, C, D, E, F, G, H, J, L, M, P, Q = 63

Path 4: A, B, C, D, E, F, G, I, J, L, M, P, Q = 64

Path 5: A, B, C, D, E, F, G, H, J, L, M, O, Q = 65

Path 6: A, B, C, D, E, F, G, I, J, L, M, O, Q = 66

Critical path: path 6
